




GlowNest

30-Day Kickoff Plan

Path to 3x ROAS by Month 3


Kickoff Plan — Days 1-30

COMMUNICATION MATRIX

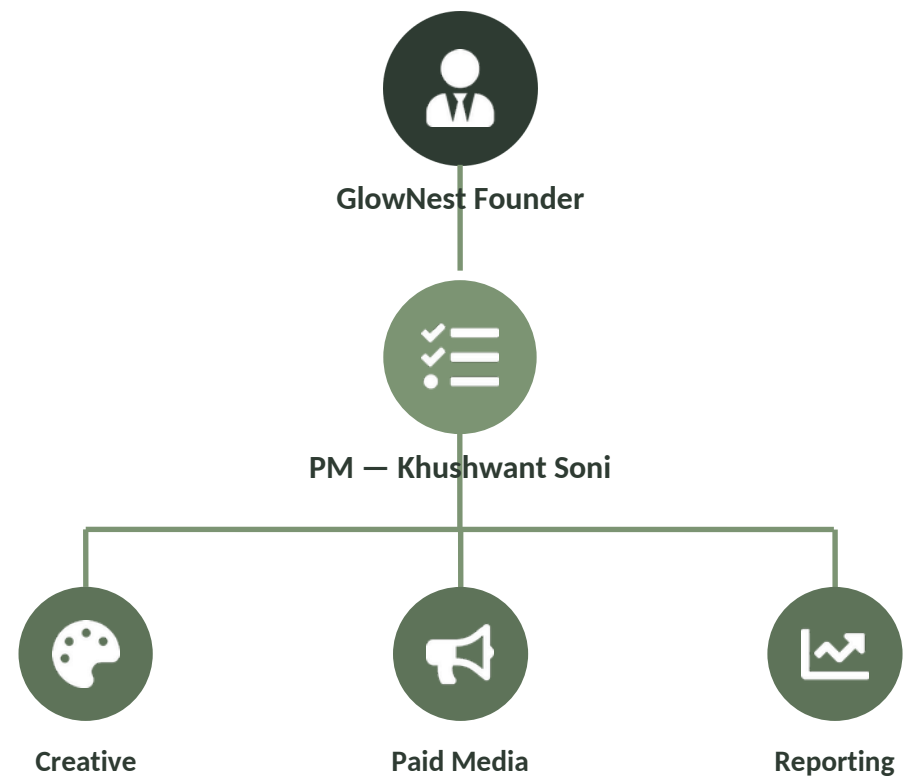

Reports to → escalation flows upward; Stakeholders are informed at each stage


WEEK-BY-WEEK MILESTONES

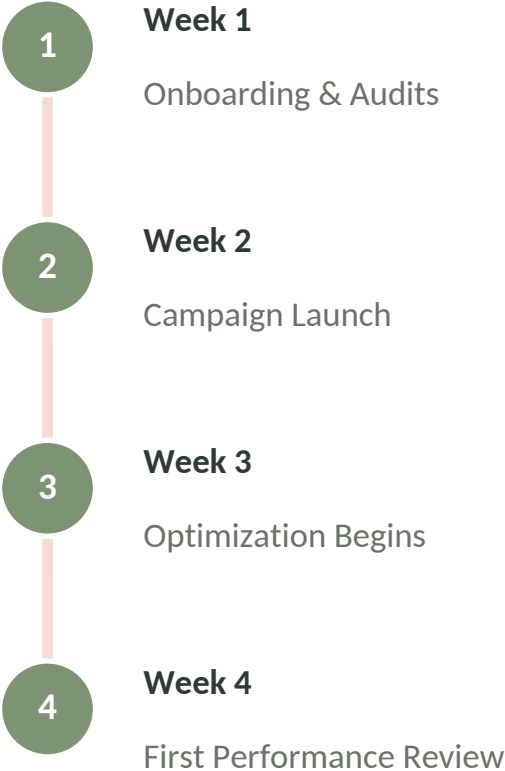

Full task-level detail and owners are tracked in Asana — linked from the project hub

Risk Register — Path to 3x ROAS

● High ● Medium ● Low

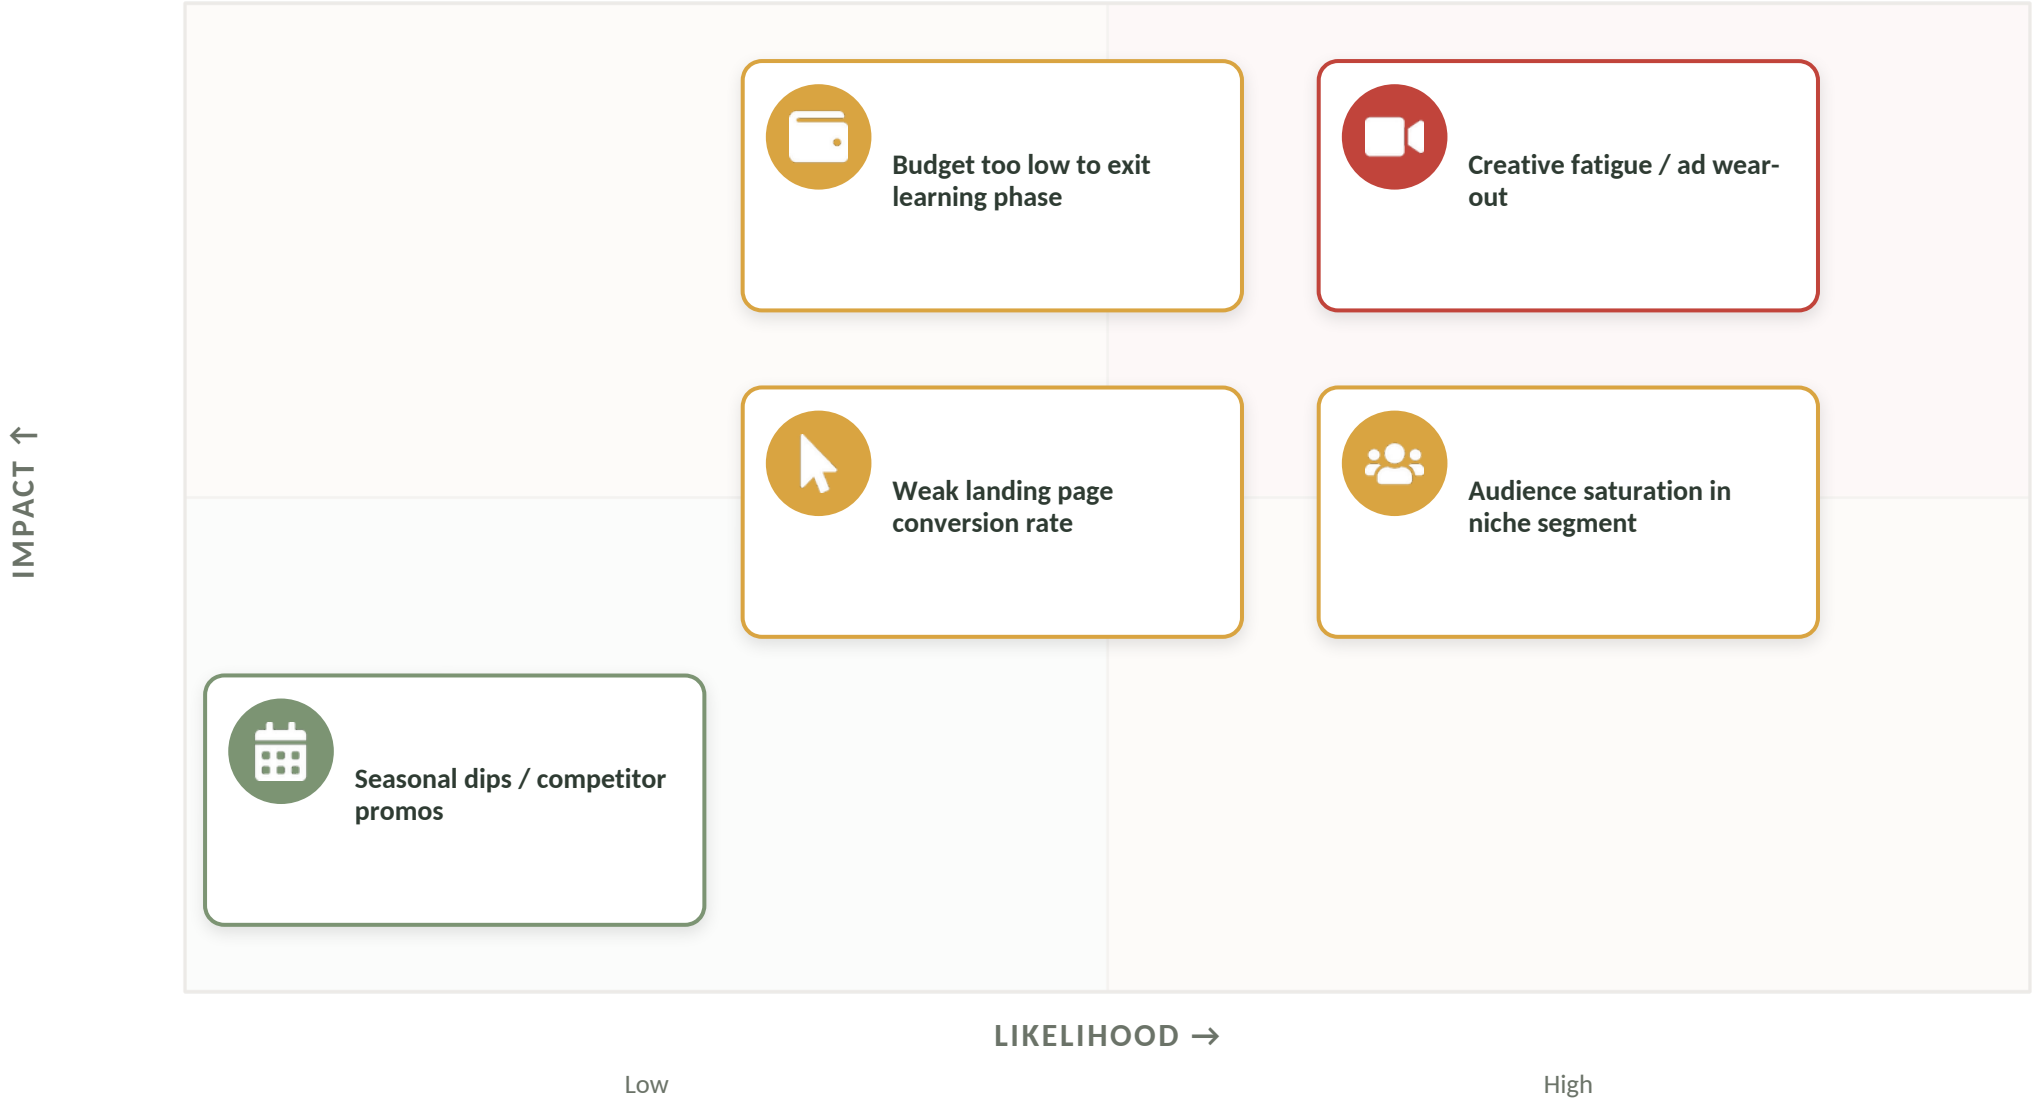

Monthly Performance — October 2026

Month 2 of 3 • Tracking toward 3.0x ROAS target



\$45.2K
Total Revenue

+22% vs. last month



845
New Customers

+15% vs. last month



32.5K
Website Traffic

+30% vs. last month



2.4x
Current ROAS

On track for 3.0x

What's Working — And What's Next

WHAT WORKED



Front-loaded budget pushed 4/5 campaigns out of the learning phase



Behavioral targeting layer lifted add-to-cart rate by 12%

NEEDS ATTENTION



Morning Routine video CTR fell below 0.8% by day 14 — fatigue



Landing page CVR at 1.3%, below the 1.5% baseline floor

NEXT MONTH'S PLAN



A/B test hero image & CTA to lift CVR above 1.5%



Roll out 5 new UGC ad creatives to fight fatigue



Stage "End of Summer Bundle" as a contingency offer

Action Items

TASK		OWNER	DEADLINE	PRIORITY
A	Run CRO audit & launch landing page A/B test	Ananya S.	Aug 25	High
R	Deliver 5 new video creatives for ad rotation	Rahul K.	Aug 27	High
V	Build audience overlap report for new targeting	Vikram M.	Aug 29	Medium
P	Set up competitor price-tracking dashboard	Priya R.	Sept 2	Low

Handling Scope Creep — Mid-Campaign WhatsApp Request



TO THE CLIENT

"Thanks for thinking of us for WhatsApp marketing! Just to flag — this falls outside our current scope. Can we schedule 20 minutes this week to scope it properly, with a short proposal on timeline and budget?"



TO THE MANAGER

Founder asked for WhatsApp marketing — not in the SOW, and capacity is tight mid-Month 2.

Recommended approach:

- Respond positively, don't commit yet
- Draft a change order with scope, deliverables, hours
- Confirm team capacity before proposing a start date



Acknowledge



Draft SOW



Confirm Capacity



"A great PM is a bridge between what the client wants and what the team can realistically deliver."



The Conflict

Client wants 3 major deals closed in 3 days —
the team can't do it without burning out



The Key Question

"If we can only finish one by Friday, which one
matters most?"



The Compromise

Nail the priority deal by Friday; finish the other
two early the following week



3x ROAS by Month 3

That's the target. Here's the plan to hit it — on time, on budget, on strategy.

Khushwant Soni

Project Manager—GlowNestAccount,HavStrategy
